

Engineering Change Notice(ECN)

ECN-D-2602-02

(Requirement for Particle optimization of cable tray near FFU)

FA연구소 설계1팀

작성	검토	승인
조현준 프로	주성진 팀장	이태경 본부장
02/05	02/05	02/05

NINEBELL

1. Engineering Change Request

NINEBELL	설계 변경 요청서(ECR) (Engineering Change Request)			Customer	AOI
				ECR No.	

Requesting department	Name / Department	/	Change ITEM	☐ Customer Requst ☐ Cost reduction ☐ Quality improve ☑ Work Efficiency ☐ Parts discontinued ☐ ETC
	Date	2025-11-27		

Request project	Category	Project Type	변경 Level (Change Level)		
	☐ MP ☐ EL	ALL 804/1204 PROCESS ROBOT		☑ Level 1	Design structure changes are required
				☐ Level 2	Simple part and work method change

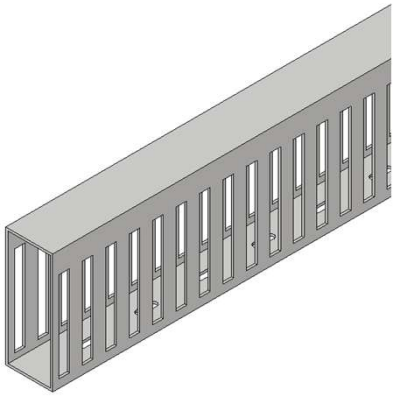
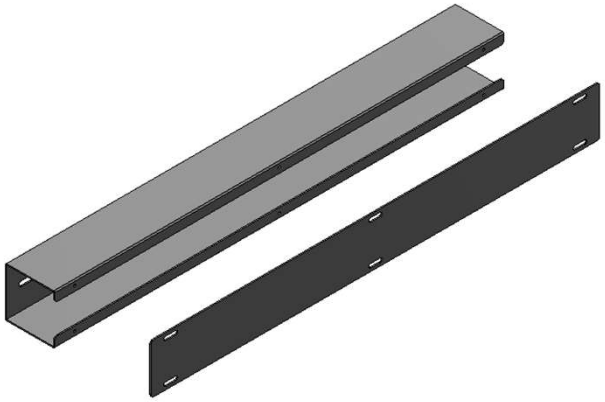
Before(Problems and Change Requests)	After(Expected Effect)
According to on-site feedback, particulate accumulation was found inside the cable trays near the FRU on the process robot.The specific location is shown in the following figure. Please help evaluate such issues and provide reasonable solutions.	



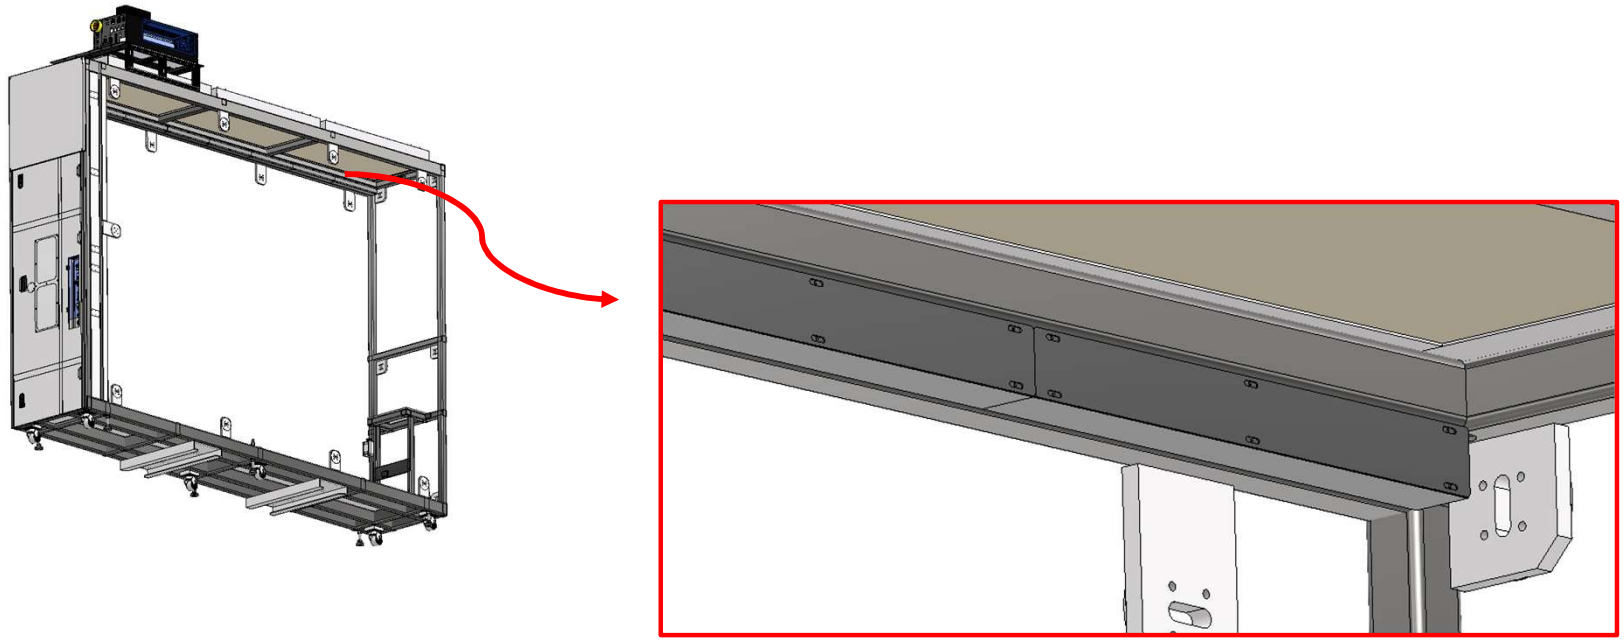


Related Division	Potential issue
☑ Mechanical design	☐ Instrument & tool additional cost incurred
☐ Electrical design	☐ Work process change and work time
☐ Manufacturing	☐ Mechanical failure
☐ Purchasing & Materials	☐ ETC
☐ Quality	

2. Engineering Change Notice

적용 장비 타입 Applicable project type	12CH HIZ PROCESS, 12CH HIZ-N PROCESS [328-20724, 328-20884]	적용 범위 Scope	■ 신규 발주분 (New order) □ 기발주분 (Previous order) □ 기출하장비 (Existing shipped equipment)
변경 사유 Reason for change	■ 고객 요청 (Customer request) □ 품질개선 (Quality improve) □ 원가절감 (Cost reduction) □ 생산성 향상 (Increase productivity) □ 부품 단종 (Part discontinuation) □ 기타 (ETC)	ECR NO.	N/A
		ECN NO.	ECN-D-2602-02
변경 상세 사유 Detailed reason for change	ACM 현장에서 FFU 근처 CABLE TRAY 내부에 파티클이 발생하여 개방형 덕트를 밀폐형 SUS 커버로 변경합니다. Particles occur inside the cable tray near the FFU, changing the open duct to a closed SUS cover		
변경 사항 Changes	변경 전(Before)	변경 후(After)	
			
상세내용 Detail	- Open Duct	- Part No : CM0HP-F100-P001-0 & CM0HP-F100-P002-0 - Closed SUS Cover	

2. Engineering Change Notice

전체 이미지 Full Image	 ※변경 위치 혹은 관련 위치 표시 ※Show changes or related positions

유효성 검토 결과 Test Result	검토 여부 Test or not	Y / N	유효성 검토 부서 Department	N/A	고객 승인 여부 Customer approval	Y / N
승인 날짜 Approval date	1. Ninebell : 2026.02.10 2. Customer : 2026/02/27		나인벨 승인 Ninebell approval	QC 2026.02.19 PASS	고객사 승인 Customer approval	
적용 일자 Effective date	2026.01.20		최초 적용 장비 Initially Applied Equipment	ZJ90-117~		
