Engineering Change Notice(ECN)

ECN-D-2607-03

(ECP MAP4 EFEM FRAME PART CHANGE)

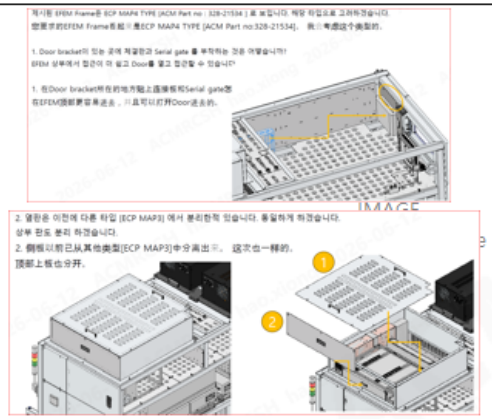
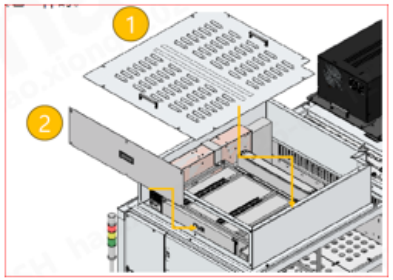
FA Research ME 2 Team

Written	Review	Confirm
곽수민 프로	최동수 팀장	이태경 본부장
7/10	07/10	07/10

NINEBELL

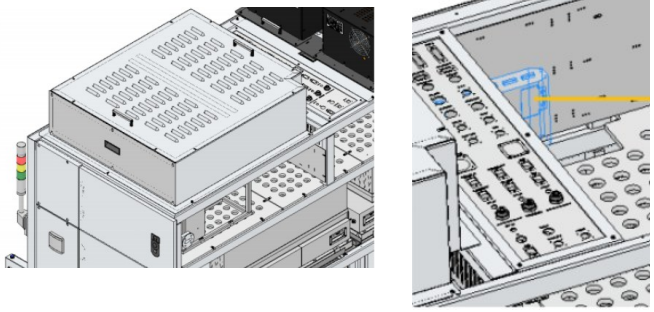
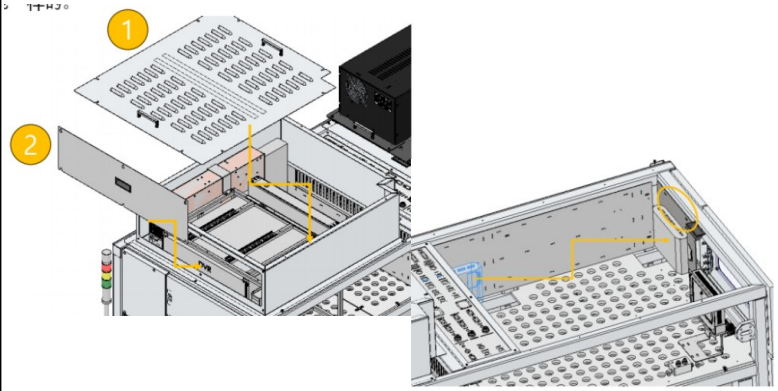
1. Engineering Change Request

Requesting department	Date	2026.6.12	Change ITEM	☐ Customer ☐ Cost ☐ Improve ☐ Efficiency ☑ ETC		
Request project	Category	Project Desc.	Type	변경 Level (Change Level)	☐ Level 1	Design structure changes are required
	☐ MP ☐ ES	ECP345	map		☐ Level 2	Simple part and work method change

Before(Problems and Change Requests)	After(Expected Effect)
	 It is necessary to change the position of the EFEM loadport controller and modify the top cover to a split type.

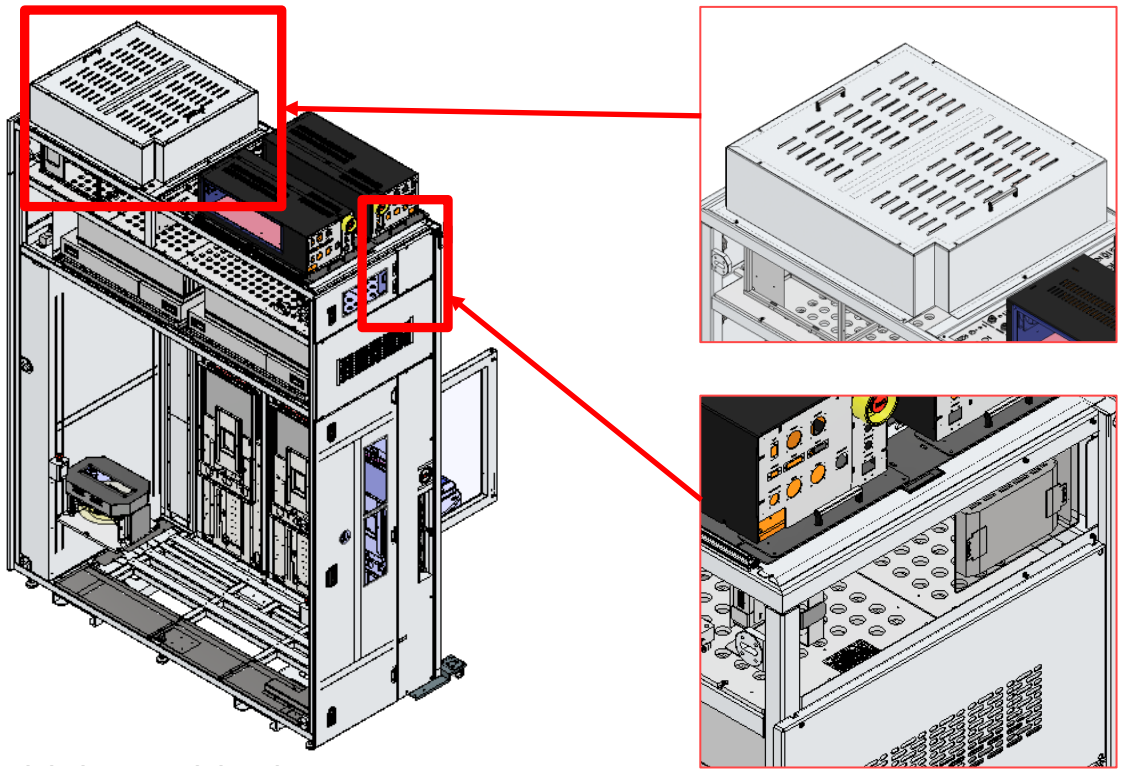
Related Division		Potential Issue	
☑	Mechanical design	☐	Instrument & tool additional cost incurred
☐	Electrical design	☐	Work process change and work time
☑	Manufacturing	☑	Mechanical failure
		☐	ETC

2. Engineering Change Notice

적용 장비 타입 Applicable project type	ECP MAP4 TYPE	적용 범위 Scope	■ 신규 발주분 (New order) □ 기발주분 (Previous order) □ 기출하장비 (Existing shipped equipment)
변경 사유 Reason for change	□ 고객 요청 (Customer request) □ 품질개선 (Quality improve) □ 원가절감 (Cost reduction) □ 생산성 향상 (Increase productivity) ■ 부품 단종 (Part discontinuation) □ 기타 (ETC)	ECR NO.	ECR-S-2606-09
		ECN NO.	ECN-D-2607-03
변경 상세 사유 Detailed reason for change	고객사의 현장 작업 중 요청사항 반영, 1. 시리얼 게이트 판 추가 및 체결 홀 추가 2, ACM RACK COVER BOX 설계 변경 Reflecting the customer's on-site request: 1. Added the Serial Gate Plate and its mounting holes. 2. Modified the ACM Rack Cover Box design.		
변경 사항 Changes	변경 전(Before)	변경 후(After)	
			
상세내용 Detail	-	➔ 시리얼 게이트 장착 판 추가 ➔ 상부 박스, 윗면에서 열수 있는 구조로 변경. ➔ Addition of the Serial Gate Plate. ➔ Upper Box redesign for top-side access.	

CONFIDENTIAL

3. Engineering Change Notice

전체 이미지 Full Image	 ※변경 또는 관련 위치 표시 ※Show changes or related positions

유효성 검토 결과 Test Result	검토 여부 Test or not	Y / (N)	유효성 검토 부서 Department	N/A	고객 승인 여부 Customer approval	Y / (N)
승인 날짜 Approval date	1. Ninebell : 2026.07.16 2. Customer : / /		나인벨 승인 Ninebell approval	QC 2026.07.16 PASS	고객사 승인 Customer approval	ACM Confirms ECP MAP team XiongHao 2026/07.23
적용 일자 Effective date	2026.07.02		최초 적용 장비 Initially Applied Equipment	ECP345, ECP346		

4. Attachments

Part No.		
Before	→	After
EE231-F1000-2	→	EE231-F1000-3
EEMP4-F00P3-0	→	EEMP4-F00P3-1
	→	EEMP4-F00P5-0
X	→	EE231-F00P7-0
X	→	I-07-008

CONFIDENTIAL
