Engineering Change Notice(ECN)

ECN-D-2608-04(Requirement for adding threaded holes)

FA Research ME 1 Team

Written	Revoew	Confirm
조현준 프로	주성진 팀장	이태경 본부장
08/19	08/19	08/19

NINEBELL

1. Engineering Change Request

NINEBELL	설계 변경 요청서(ECR) (Engineering Change Request)			Customer	ACM
				ECR No.	

Requesting department	Name / Department	/	Change ITEM	☑ Customer Requst ☐ Cost reduction ☐ Quality improve ☐ Work Efficiency ☐ Parts discontinued ☐ ETC
	Date	2026-08-05		

Request project	Category	Project Type	변경 Level (Change Level)		
	☐ MP ☐ ES	ALL 8/12CH SINGLE CLEAN EFEM AND process robot	☑ Level 1	Design structure changes are required
			☐ Level 2	Simple part and work method change

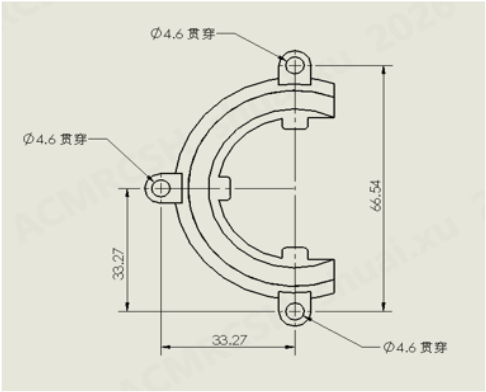
Before(Problems and Change Requests)

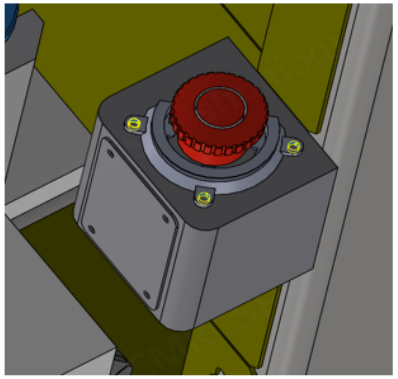
Our MFG department reported that there are no screw holes on the EMS button to secure the cover,requiring our MFG engineers to manually drill screw holes for each project.



After(Expected Effect)

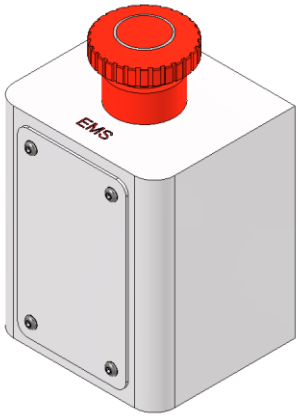
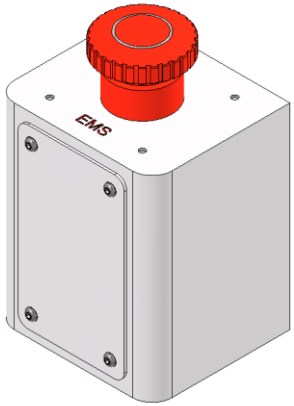
For subsequent EFEM and process robot,we would like to add three M3 threaded holes on the EMS button.Please refer to the figure below for the specific locations.





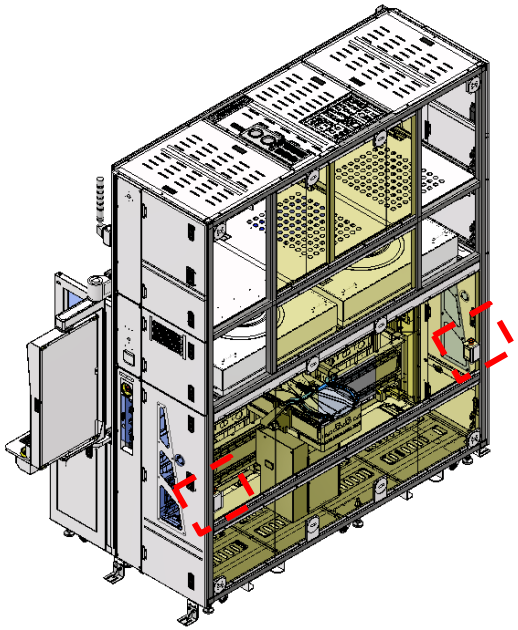
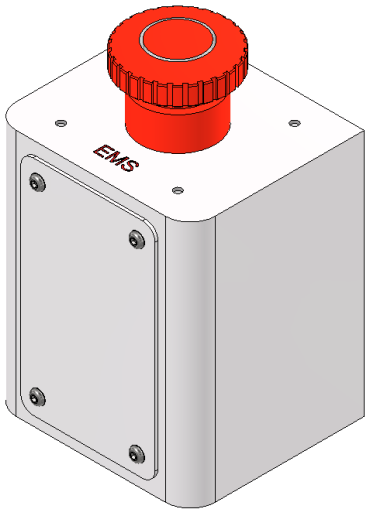
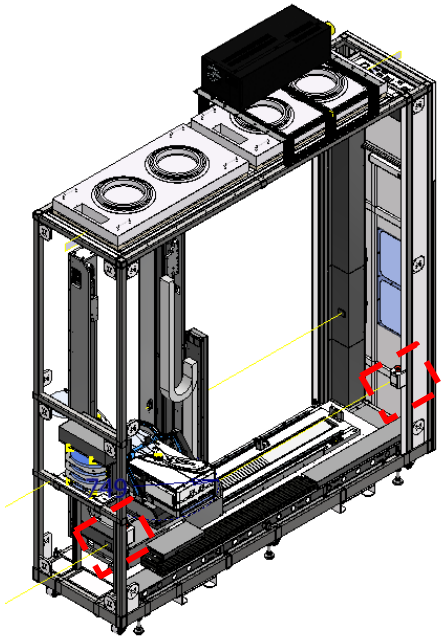
Related Division		Potential Issue	
	☑ Mechanical design		☐ Instrument & tool additional cost incurred
	☐ Electrical design		☐ Work process change and work time
	☐ Manufacturing		☐ Mechanical failure
	☐ Purchasing & Materials		☐ ETC
	☐ Quality		

2. Engineering Change Notice

적용 장비 타입 Applicable project type	[Clean Type] ALL 8CH & 12CH	적용 범위 Scope	■ 신규 발주분 (New order) □ 기발주분 (Previous order) □ 기출하장비 (Existing shipped equipment)
변경 사유 Reason for change	■ 고객 요청 (Customer request) □ 품질개선 (Quality improve) □ 원가절감 (Cost reduction) □ 생산성 향상 (Increase productivity) □ 부품 단종 (Part discontinuation) □ 기타 (ETC)	ECR NO.	ECR-S-2608-011
		ECN NO.	ECN-D-2608-04
변경 상세 사유 Detailed reason for change	• 고객사용 EMS 버튼의 베젤을 체결하기 위한 TAP 추가. • Added tapped holes for mounting the EMS button bezel for the customer.		
변경 사항 Changes	변경 전(Before)	변경 후(After)	
			
상세내용 Detail	- PN : DP-170P1-1(MIR)	- PN : DP-170P1-2(_MIR)	

CONFIDENTIAL

2. Engineering Change Notice

전체 이미지 Full Image	<EFEM>   <PROCESS>  ※변경 위치 혹은 관련 위치 표시 ※Show changes or related positions

유효성 검토 결과 Test Result	검토 여부 Test or not	Y / (N)	유효성 검토 부서 Department	N/A	고객 승인 여부 Customer approval	(Y) / N
승인 날짜 Approval date	1. Ninebell : 2026.08.21 2. Customer : / /		나인벨 승인 Ninebell approval	QC 2026.08.21 PASS	고객사 승인 Customer approval	ACM confirms ShuaiXu 2026/08/24
적용 일자 Effective date	2026.08.21~(PO)		최초 적용 장비 Initially Applied Equipment	MISC-8CH BS #4		

CONFIDENTIAL
